

# River Corridor Closure

Safety • People • Results

## Subcontracting Overview *and Lessons Learned*

**John Fulton**

Washington Closure Hanford




U.S. Department of Energy  
Richland Operations Office

# Contract Scope

## ***Cleanup of the 218 square mile River Corridor***

- Demolish 486 buildings
- Safe storage of four reactor blocks
- Cleanup of 370 waste sites
- Disposal of four million tons of contaminated material

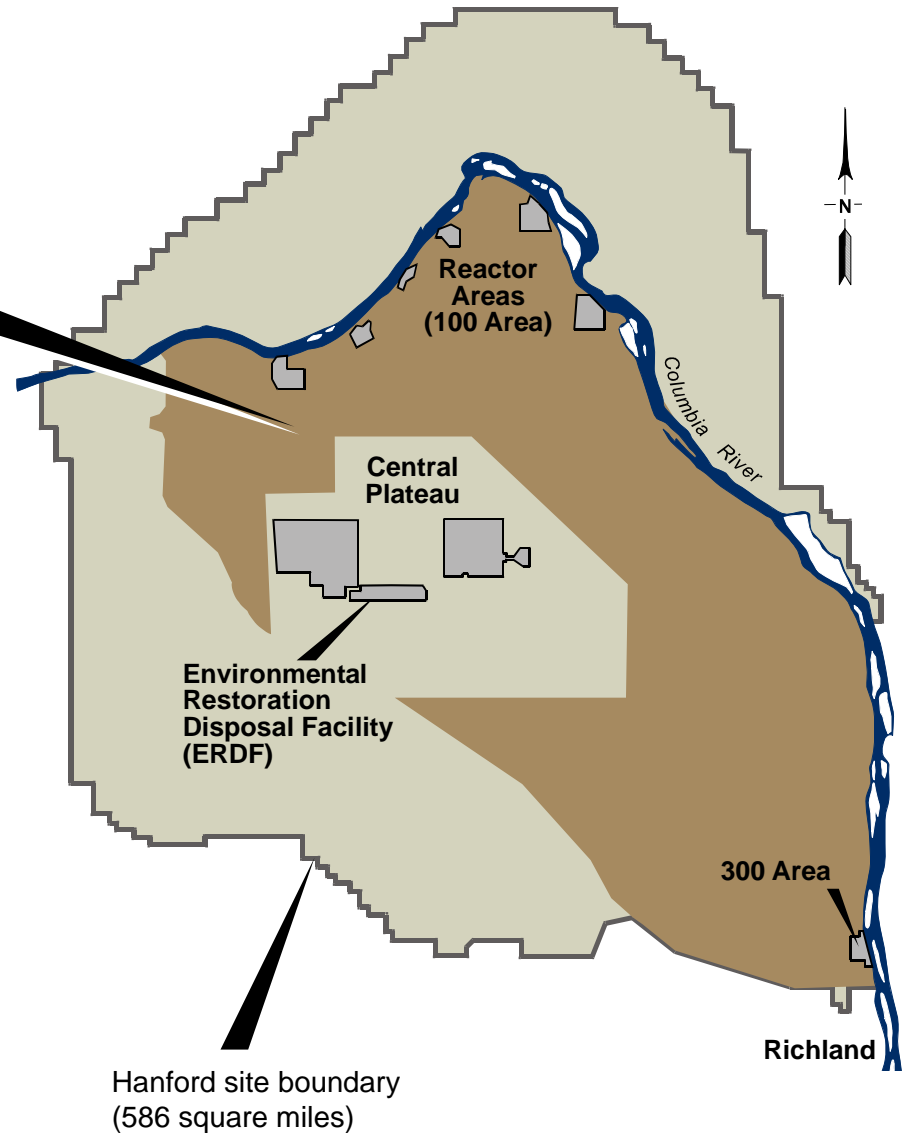


# Subcontracting Opportunities

- Clean building demolition
- Explosive demolition
- Technical services
- Materials, supplies, equipment
- Hazardous waste removal
- Sampling
- Soil excavation and backfill
- Landfill construction for future expansion



# FY06 WCH Procurement by Commodity

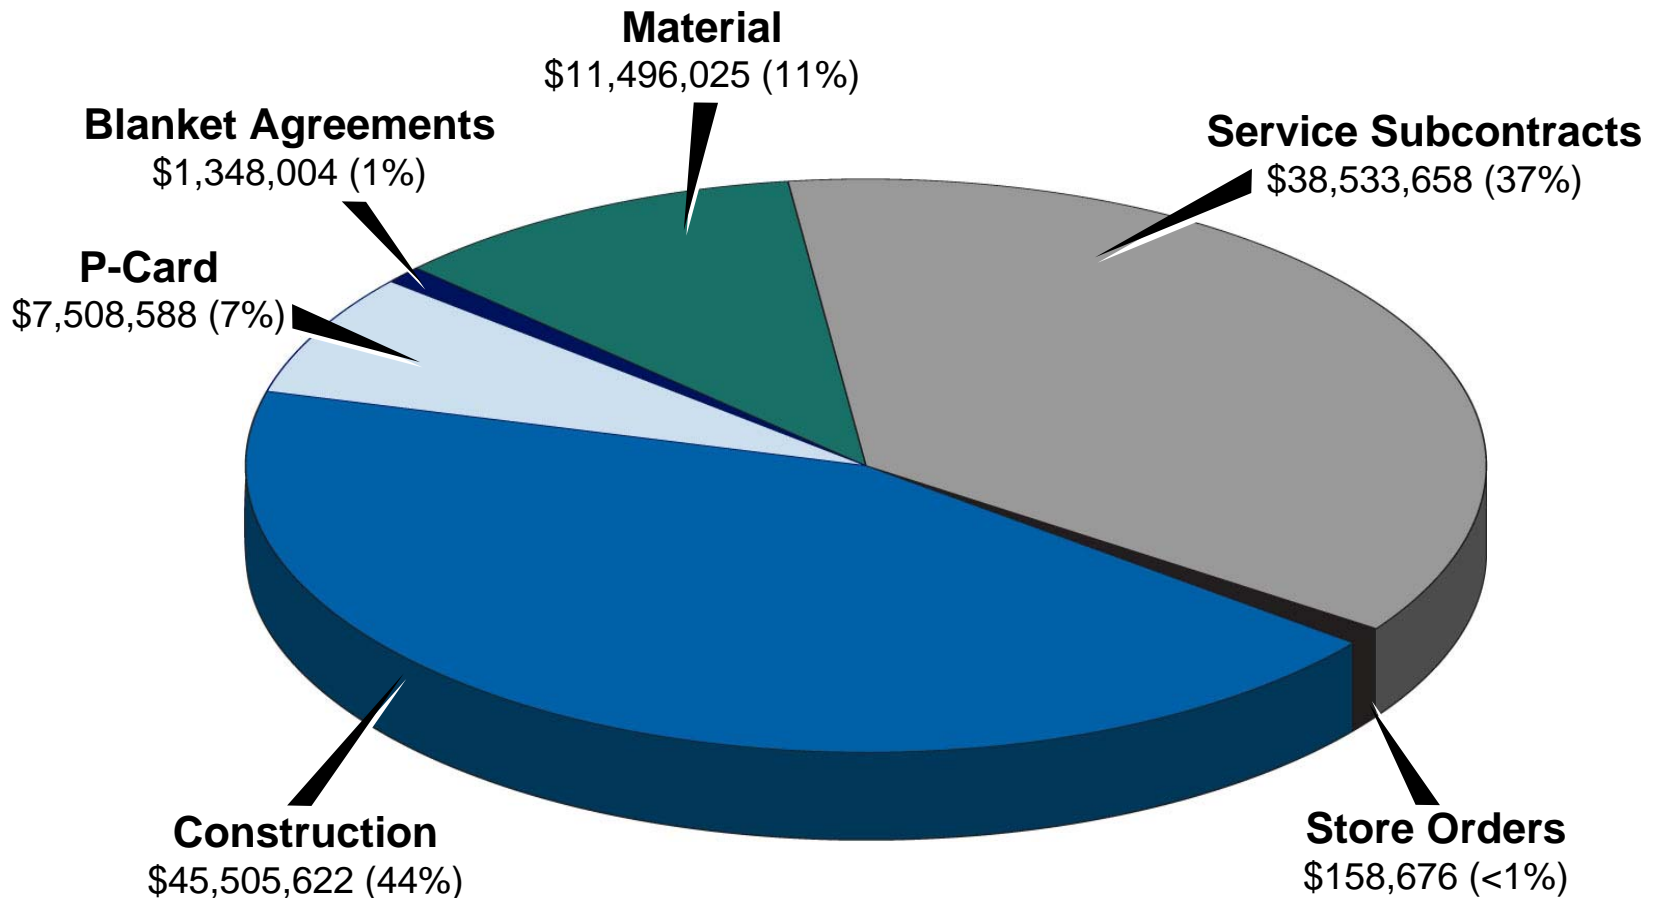

**Total = \$104,550,573**




# Lessons Learned

- Financial systems
  - Accurate and timely pricing for changes
  - Cash flow
- Understanding **all** details of the bid
- Bonding requirements – construction vs. environmental
- Contract award schedules are subject to change
- Contract awards, modifications, changes, **must** come through the WCH Procurement office
- Expanded use of P-Card

*Key  
Elements  
for  
Success*

- Qualified and experienced key personnel
  - Project manager
  - Safety/industrial hygiene manager
- Excellent safety record
- Solid financial systems
- Demonstrated technical expertise
- Good past performance
- Technical innovation

# FY06 Procurement Goals vs. Actuals

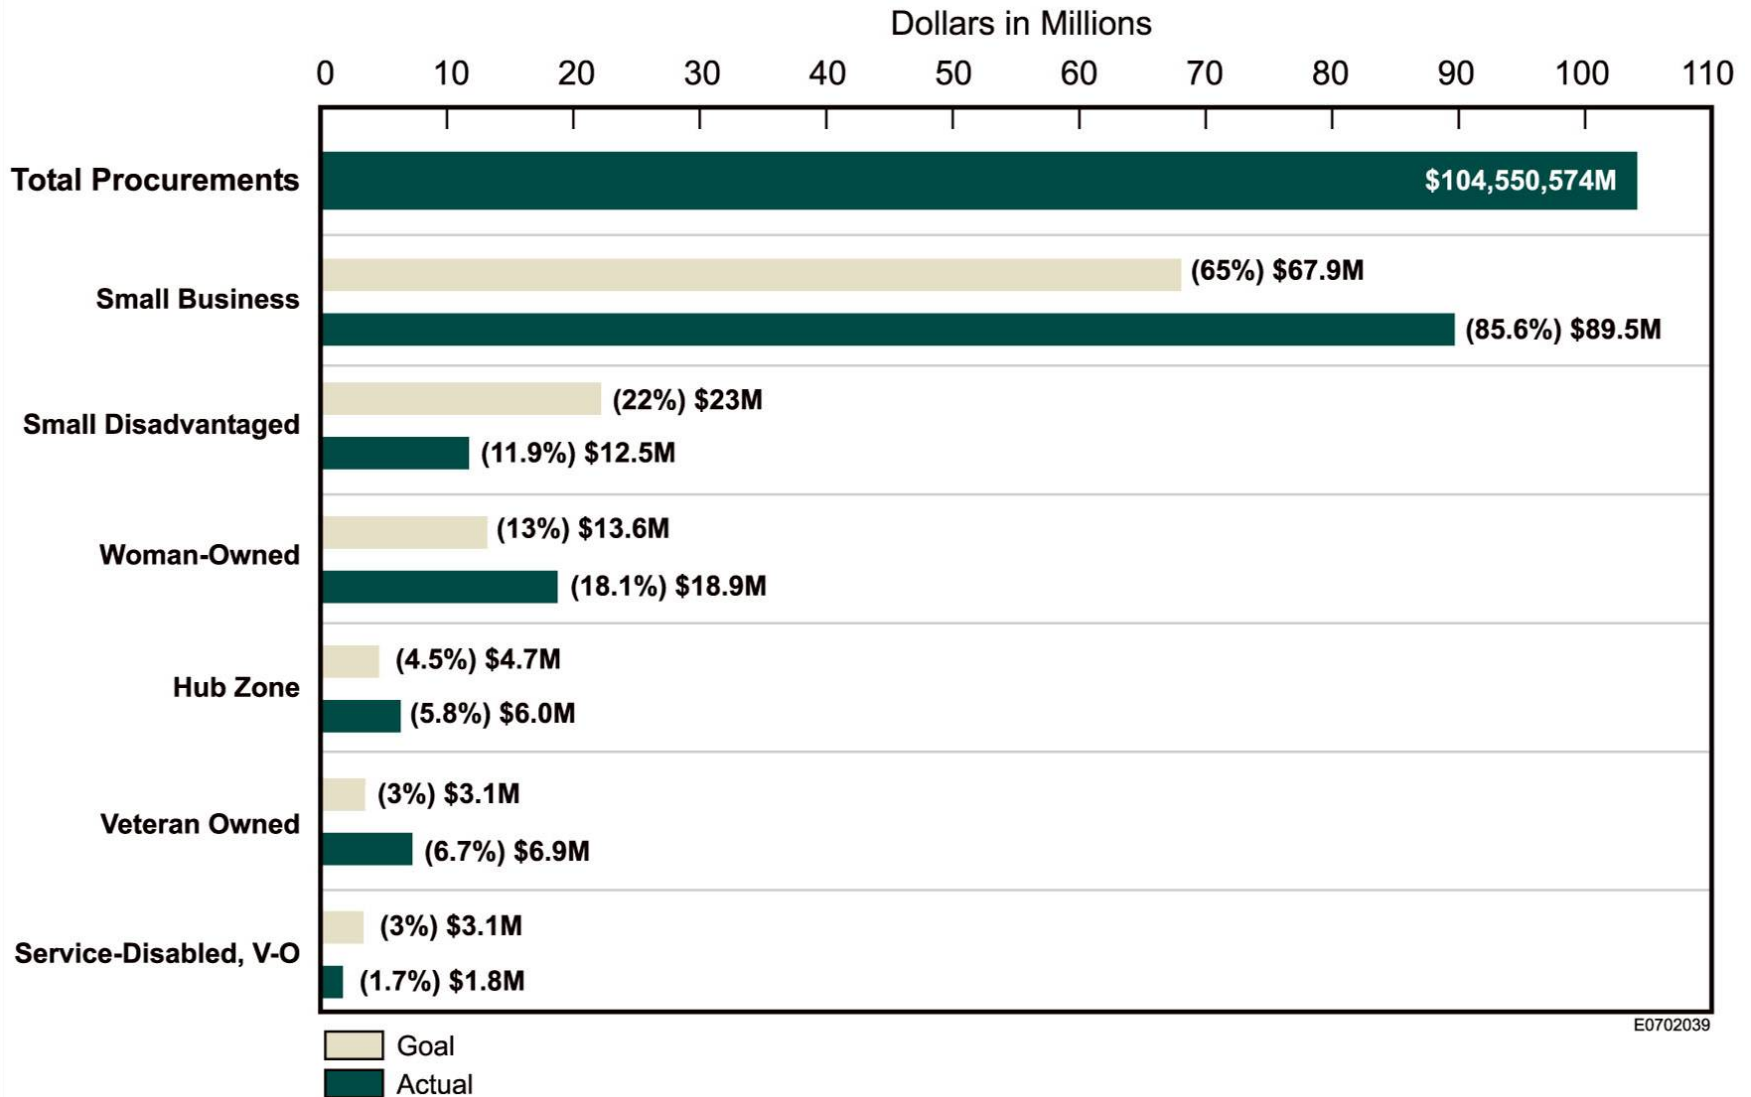

# FY07 Procurement Plans

## **Waste Disposal Operations**

ERDF construction quality assurance

Construct ERDF cells 7 & 8

Design/construct ERDF cover for  
ERDF cells 3 & 4

## **Award date**

July 2007

July 2007

April 2007

## **Waste Site Cleanup**

100 H remediation

## **Award date**

May 2007

## **Building Demolition**

Temporary facilities construction

## **Award date**

Potential late FY07



# Procurement Information and Contacts

## **90-Day Forecast of Anticipated WCH Projects**

*<http://www.washingtonclosure.com/procure/90-day.html>*

## **Supplier/Contractor Questionnaire**

*<http://www.washingtonclosure.com/procure/supplier.html>*

## **WCH Major Subcontractor Listing**

*<http://www.washingtonclosure.com/procure/forms/majorsubs.doc>*

## **Questions/Comments**

*[supplierforum@wch-rcc.com](mailto:supplierforum@wch-rcc.com)*

## **Small Business Representative**

Tess Klatt

509-372-9522

*[taklatt@wch-rcc.com](mailto:taklatt@wch-rcc.com)*
